


Delhi – Mumbai Expressway


Status as of September 30th, 2022
(Length in km)

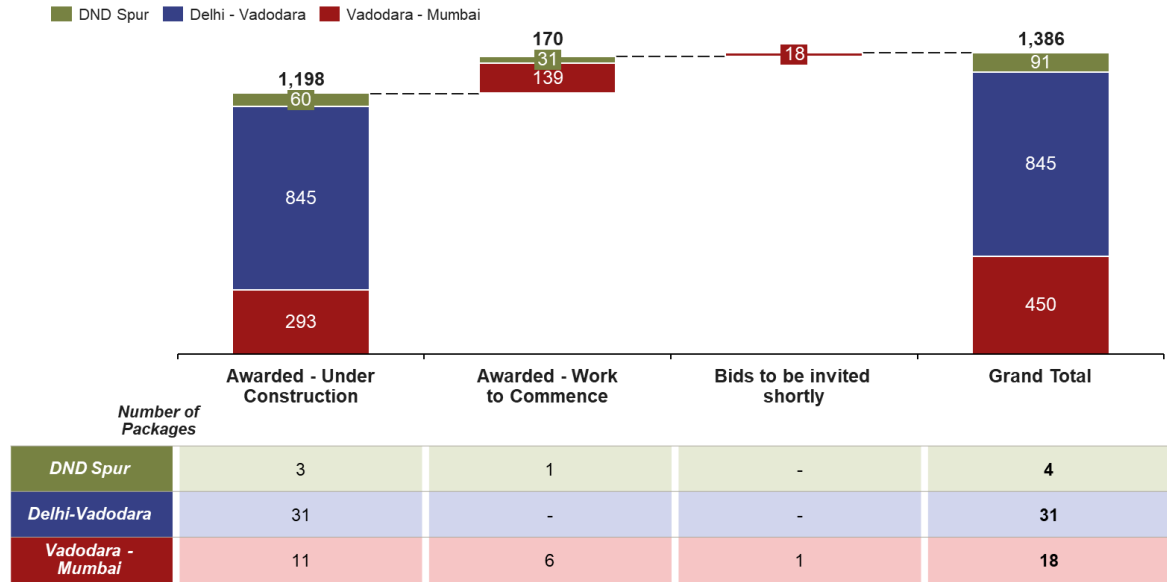


Number of Packages	Awarded - Under Construction	Awarded - Work to Commence	Bids to be invited shortly	Grand Total
	DND Spur	3	1	-
Delhi-Vadodara	31	-	-	31
Vadodara - Mumbai	11	6	1	18

Key Plan (Status as of September 26th, 2022)


Delhi - Vadodara Section (Including Delhi-Faridabad-Sohna)

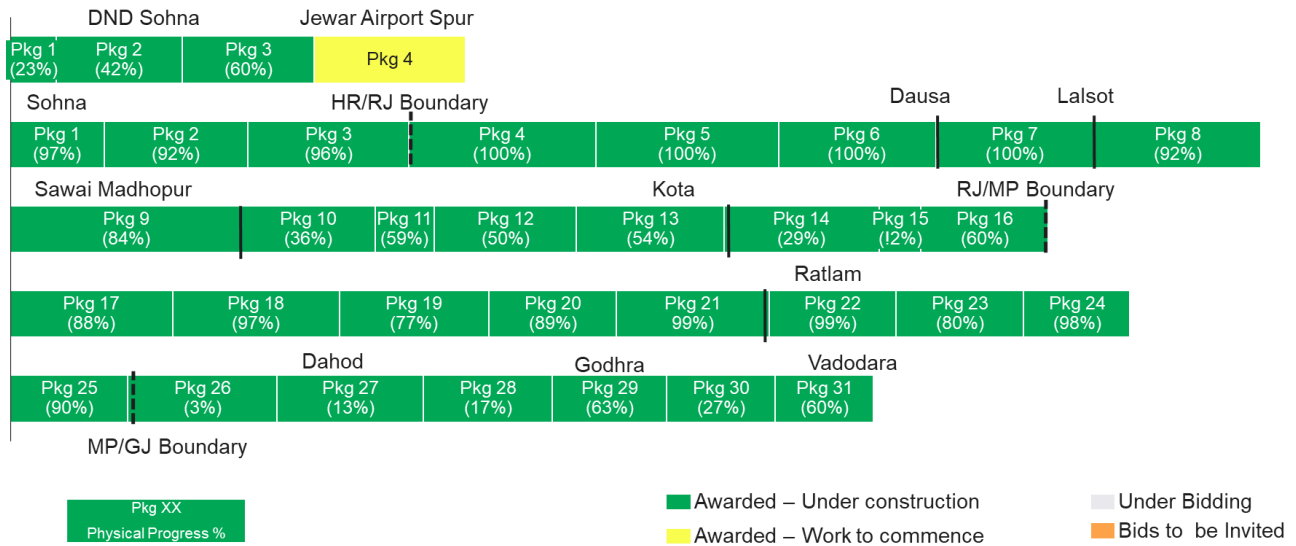

Vadodara – Mumbai (Virar) Section



Spur to JNPT

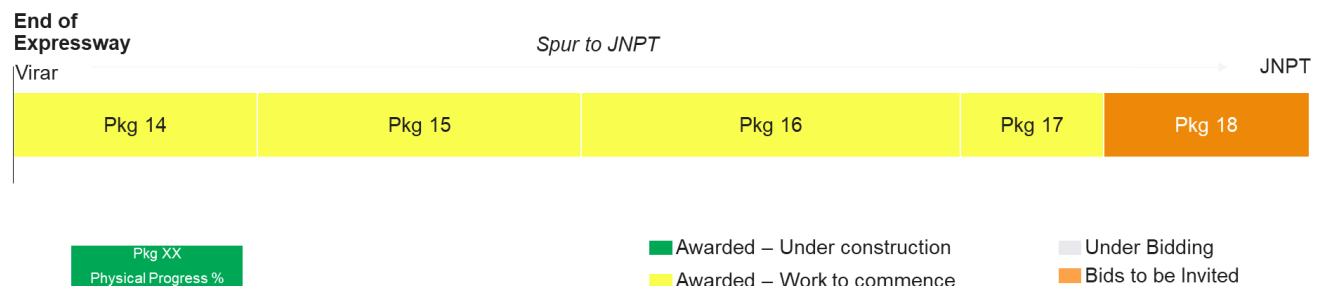

Delhi – Mumbai Expressway Package Level Status (as of September 26th, 2022)

#	State	Package	Chainage		Length (km)	Status	Award Date	Date of Commencement	Scheduled Completion Date	Concessionaire	Physical Progress (%)
			From	To							
1	Haryana	Pkg 1	0.000	9.000	9	Under Construction	31-Jul-20	11-Jan-22	12-Jan-24	M/s Dineshchandra R. Agrawal Infracon Pvt. Ltd.	23%
2	Haryana	Pkg 2	9.000	33.000	25	Under Construction	30-Jul-20	10-Aug-21	11-Aug-23	M/s Dineshchandra R. Agrawal Infracon Pvt. Ltd.	42%
3	Haryana	Pkg 3	33.000	59.063	26	Under Construction	07-Aug-20	14-May-21	15-May-23	M/s Dineshchandra R. Agrawal Infracon Pvt. Ltd.	60%
s4	Uttar Pradesh	Jewar Connectivity	0	30	31	Awarded - Work to Commence	01-Aug-22	-	-	M/s APCO Infratech Pvt. Ltd.	-
Delhi – Faridabad - Sohna Total					90						
1	Haryana	Pkg 1	0.000	18.460	18	Under Construction	05-Mar-19	13-Sep-19	30-Oct-22	M/s APCO Infratech Pvt. Ltd.	97%
2	Haryana	Pkg 2	18.460	46.960	29	Under Construction	05-Mar-19	13-Sep-19	30-Oct-22	M/s APCO Infratech Pvt. Ltd.	92%
3	Haryana	Pkg 3	46.960	78.760	32	Under Construction	28-May-19	05-Sep-19	30-Oct-22	M/s Centrodorstroy India Pvt. Ltd.	96%
4	Rajasthan	Pkg 4	78.760	115.660	37	Under Construction	09-Mar-19	10-Dec-19	30-Oct-22	M/s H.G. Infra Engineering Limited	100%
5	Rajasthan	Pkg 5	115.660	151.800	36	Under Construction	09-Mar-19	10-Dec-19	30-Oct-22	M/s KCC Buildcon Pvt. Ltd.	100%
6	Rajasthan	Pkg 6	151.800	182.960	31	Under Construction	09-Mar-19	20-Nov-19	30-Oct-22	M/s KCC Buildcon Pvt. Ltd.	100%
7	Rajasthan	Pkg 7	182.960	214.220	31	Under Construction	28-May-19	07-Feb-20	30-Oct-22	M/s Gawar Constructions Ltd.	100%
8	Rajasthan	Pkg 8	214.220	247.270	33	Under Construction	11-Feb-20	07-Nov-20	31-Mar-23	M/s H.G. Infra Engineering Limited	92%
9	Rajasthan	Pkg 9	247.270	292.910	46	Under Construction	26-Feb-20	18-Dec-20	31-Mar-23	M/s H.G. Infra Engineering Limited	84%
10	Rajasthan	Pkg 10	292.910	319.360	26	Under Construction	30-Jun-20	22-May-21	31-Mar-23	M/s Dhaya Maju Infrastructure (Asia) Sdn. Berhad - Crescent EPC Projects & Technical Services Ltd.	36%
11	Rajasthan	Pkg 11	319.360	330.990	12	Under Construction	19-Jun-20	22-May-21	31-Mar-23	M/s Larsen & Toubro Ltd.	59%
12	Rajasthan	Pkg 12	330.990	359.130	28	Under Construction	18-Jun-20	01-Apr-21	31-Mar-23	M/s G R Infraprojects Limited	50%
13	Rajasthan	Pkg 13	359.130	388.380	29	Under Construction	18-Jun-20	25-Mar-21	31-Mar-23	M/s CDS Infra Projects Limited	54%
14	Rajasthan	Pkg 14	388.380	418.960	31	Under Construction	30-Jun-20	24-May-21	31-Mar-23	M/s Dhaya Maju Infrastructure (Asia) Sdn. Berhad - Crescent EPC Projects & Technical Services Ltd.	29%
15	Rajasthan	Pkg 15	418.960	427.260	8	Under Construction	22-Dec-20	06-Jul-21	31-Mar-23	M/s Dilip Buildcon Ltd – M/s Altis Holding Corporation	12%
16	Rajasthan	Pkg 16	427.260	452.390	25	Under Construction	08-Jul-20	05-Jan-21	31-Mar-23	M/s Dineshchandra R. Agrawal Infracon Pvt. Ltd.	60%

#	State	Package	Chainage		Length (km)	Status	Award Date	Date of Commencement	Scheduled Completion Date	Concessionaire	Physical Progress (%)
			From	To							
17	Madhya Pradesh	Pkg 17	452.390	484.390	32	Under Construction	11-Feb-20	08-Oct-20	30-Dec-22	M/s JiangXi Construction Engineering (Group) Corporation Ltd. - MKC Infrastructure Ltd. (JV)	88%
18	Madhya Pradesh	Pkg 18	484.390	517.390	33	Under Construction	01-Oct-19	07-Feb-20	30-Dec-22	M/s G R Infraprojects Limited	97%
19	Madhya Pradesh	Pkg 19	517.390	546.890	30	Under Construction	11-Feb-20	05-Nov-20	30-Dec-22	M/s JiangXi Construction Engineering (Group) Corporation Ltd. - MKC Infrastructure Ltd. (JV)	77%
20	Madhya Pradesh	Pkg 20	546.890	572.190	25	Under Construction	08-Mar-19	06-Dec-19	30-Dec-22	M/s GHV (India) Pvt Ltd.	89%
21	Madhya Pradesh	Pkg 21	572.190	602.390	30	Under Construction	28-May-19	10-Dec-19	30-Dec-22	M/s G R Infraprojects Limited	99%
22	Madhya Pradesh	Pkg 22	602.390	627.390	25	Under Construction	19-Jun-20	20-Nov-20	30-Dec-22	M/s Larsen & Toubro Ltd.	99%
23	Madhya Pradesh	Pkg 23	627.390	652.690	25	Under Construction	07-Aug-19	29-May-20	30-Dec-22	M/s G R Infraprojects Limited	80%
24	Madhya Pradesh	Pkg 24	652.690	673.740	21	Under Construction	07-Aug-19	05-Mar-20	30-Dec-22	M/s G R Infraprojects Limited	98%
25	Madhya Pradesh	Pkg 25	673.740	696.890	23	Under Construction	07-Aug-19	05-Mar-20	30-Dec-22	M/s G R Infraprojects Limited	90%
26	Gujarat	Pkg 26	696.890	726.390	30	Under Construction	11-Nov-21	02-May-22	31-Mar-24	M/s Atlas Construction Pvt. Ltd. - NKC (JV)	3%
27	Gujarat	Pkg 27	726.390	755.390	29	Under Construction	30-Jul-21	15-Feb-22	31-Mar-24	M/s GHV (India) Pvt Ltd	13%
28	Gujarat	Pkg 28	755.390	780.890	26	Under Construction	27-May-21	16-Nov-21	31-Mar-24	M/s GHV (India) Pvt Ltd	17%
29	Gujarat	Pkg 29	780.890	803.390	23	Under Construction	23-Jul-20	16-Apr-21	31-Mar-24	M/s PNC Infratech Pvt. Ltd.	63%
30	Gujarat	Pkg 30	803.390	824.890	22	Under Construction	05-Oct-20	08-Sep-21	31-Mar-24	M/s Patel Infrastructure Limited	27%
31	Gujarat	Pkg 31	824.890	844.350	19	Under Construction	23-Jul-20	18-May-21	31-Mar-24	M/s PNC Infratech Pvt. Ltd.	60%
Delhi – Vadodara Total					845						
1	Gujarat	Pkg 1	355.000	378.740	24	Under Construction	20-Mar-18	18-Jan-19	30-Oct-22	M/s IRB Infrastructure Developers Ltd.	100%
2	Gujarat	Pkg 2	323.000	355.000	32	Under Construction	28-Mar-18	31-Jan-19	30-Oct-22	M/s IRCON International Limited	99%
3	Gujarat	Pkg 3	292.000	323.000	31	Under Construction	28-Mar-18	08-Mar-19	30-Oct-22	M/s Patel Infrastructure Limited	96%
4	Gujarat	Pkg 4	279.000	292.000	13	Under Construction	28-Mar-18	10-Dec-18	30-Oct-22	M/s Ashoka Buildcon Limited	97%
5	Gujarat	Pkg 5	254.430	279.000	25	Under Construction	28-Mar-18	01-Nov-19	31-Mar-24	M/s Sadbhav Engineering Pvt. Ltd.	22%
6	Gujarat	Pkg 6	217.500	254.430	37	Under Construction	30-Jul-20	10-Dec-21	31-Mar-24	M/s G R Infraprojects Limited	20%
7	Gujarat	Pkg 7	190.000	217.500	28	Under Construction	31-Jul-20	10-Dec-21	31-Mar-24	M/s IRB Infrastructure Developers Ltd.	14%

#	State	Package	Chainage		Length (km)	Status	Award Date	Date of Commencement	Scheduled Completion Date	Concessionaire	Physical Progress (%)
			From	To							
8	Gujarat	Pkg 8	154.600	190.000	35	Awarded - Work to Commence	27-May-21	-	31-Mar-24	M/s Roadway Solutions India Infra Ltd.	-
9	Gujarat	Pkg 9	128.000	154.600	27	Awarded - Work to Commence	30-Jul-21	-	31-Mar-24	M/s Roadway Solutions India Infra Ltd.	-
10	Gujarat	Pkg 10	103.400	128.000	25	Under Construction	30-Mar-21	21-Mar-22	31-Mar-24	M/s Roadway Solutions India Infra Ltd.	1%
11	Maharashtra	Pkg 11	77.000	103.400	26	Under Construction	15-Oct-20	28-May-22	31-Mar-24	M/s RKC Infrabuilt Private Ltd.	1%
12	Maharashtra	Pkg 12	50.700	77.000	26	Under Construction	15-Oct-20	22-Mar-22	31-Mar-24	M/s Montecarlo Limited	4%
13	Maharashtra	Pkg 13	26.582	50.700	24	Under Construction	15-Oct-20	22-Mar-22	31-Mar-24	M/s G R Infraprojects Ltd.	10%
		Pkg 13 (Spur to JNPT)	0.000	3.000	3						
Vadodara – Virar Total					355						-
1	Maharashtra	Pkg 14 (Spur to JNPT)	3.000	20.200	17	Awarded - Work to Commence	30-Nov-21	-	31-Mar-24	M/s IRCON International Limited	-
2	Maharashtra	Pkg 15 (Spur to JNPT)	20.200	43.000	23	Awarded - Work to Commence	30-Nov-21	-	31-Mar-24	M/s Agroh Infrastructre & Developer Pvt. Ltd.	-
3	Maharashtra	Pkg 16 (Spur to JNPT)	43.000	69.700	27	Awarded - Work to Commence	29-Oct-21	-	31-Mar-24	M/s Shivalaya Construction Ltd.	-
4	Maharashtra	Pkg 17 (Spur to JNPT)	69.700	79.780	10	Awarded - Work to Commence	24-Dec-21	-	31-Mar-24	M/s IRCON International Limited	-
5	Maharashtra	Pkg 18 (Spur to JNPT)	79.780	94.290	18	Bids to be Invited shortly	-	-	31-Mar-24	-	-
Virar – JNPT Total					91						
Delhi - Mumbai Total					1386						-

Photographs



8 laning and road marking completed near Vadodara, Gujarat



Clover Interchange near Bharuch, Gujarat



SMA completed near Ratlam, Madhya Pradesh



Animal Underpass construction near Sawai Madhapur, Rajasthan



Lighting and road marking completed near Ankleshwar, Gujarat



Iconic 8 lane cable stayed bridge across Narmada River near Ankeleshwar, Gujarat



Motel developed as part of WSA near Vadodara, Gujarat
