



## Delhi – Mumbai Expressway

Status as of May28<sup>th</sup>, 2021  
(Length in km)

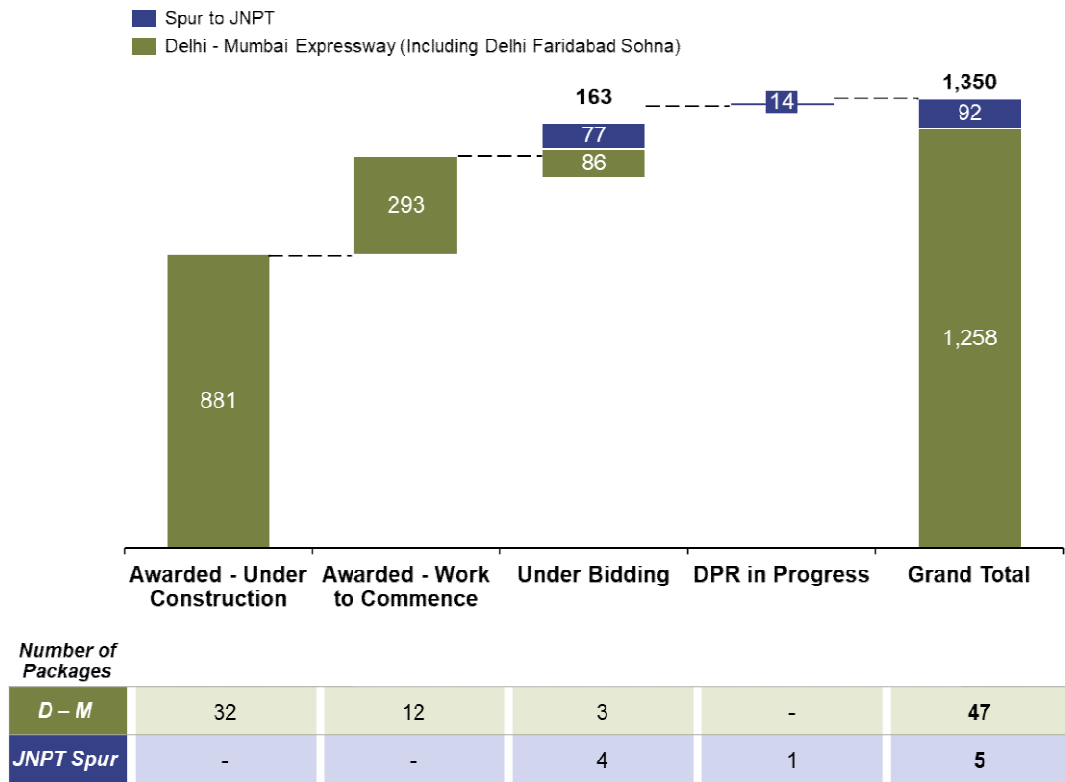


## Key Plan (Status as of May28<sup>th</sup>, 2021)


### Delhi - Vadodara Section (Including Delhi-Faridabad-Sohna)

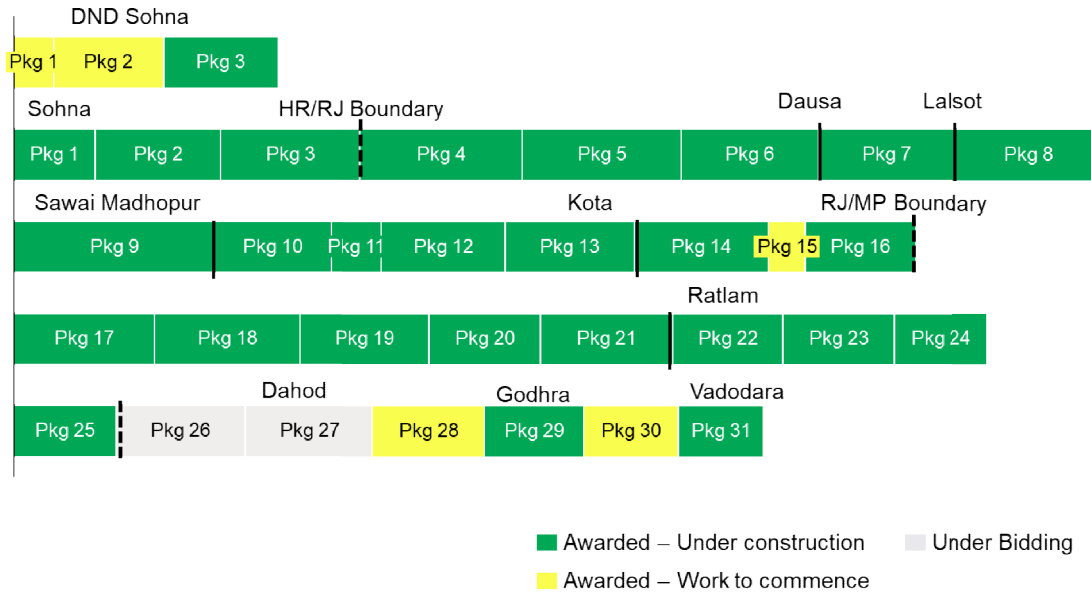

### Vadodara – Mumbai (Virar) Section

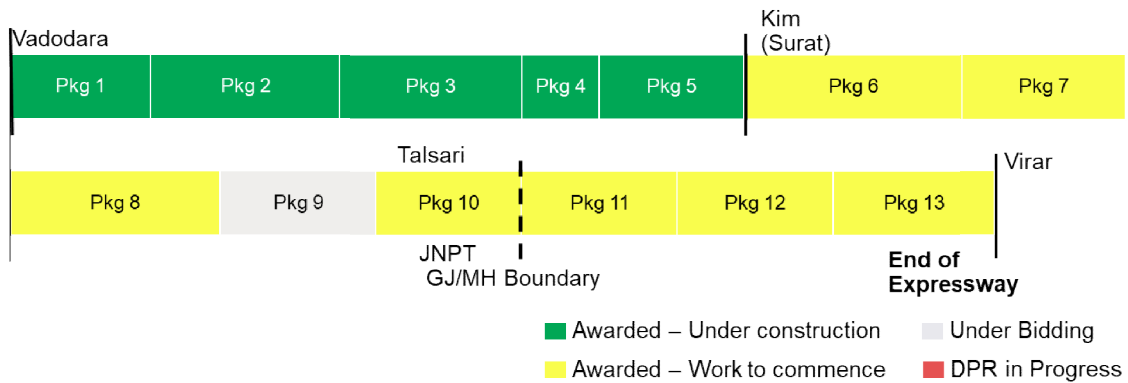

### Spur to JNPT

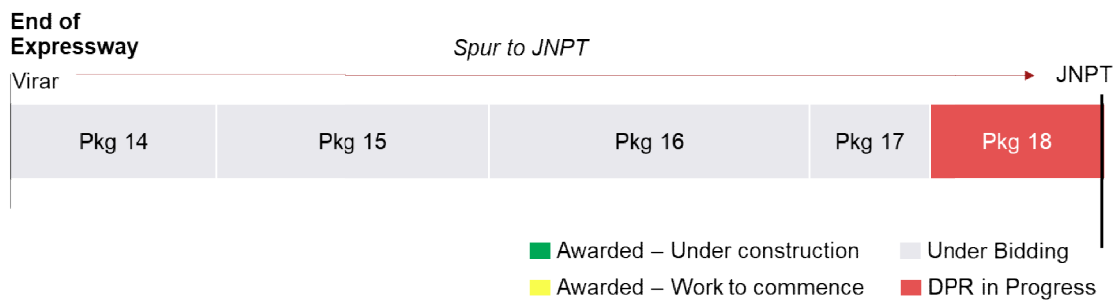

## Delhi – Mumbai Expressway Package Level Status (as of May 28<sup>th</sup>, 2021)

| #                                      | State          | Package | Chainage |         | Length (km) | Status                     | Award Date | Date of Commencement | Scheduled Completion Date | Concessionaire                                                                                      | Physical Progress (%) |
|----------------------------------------|----------------|---------|----------|---------|-------------|----------------------------|------------|----------------------|---------------------------|-----------------------------------------------------------------------------------------------------|-----------------------|
|                                        |                |         | From     | To      |             |                            |            |                      |                           |                                                                                                     |                       |
| 1                                      | Haryana        | Pkg 1   | 0.000    | 9.000   | 9           | Awarded - Work to Commence | 31-Jul-20  | -                    | -                         | M/s Dineshchandra R. Agrawal Infracon Pvt. Ltd.                                                     | -                     |
| 2                                      | Haryana        | Pkg 2   | 9.000    | 33.000  | 25          | Awarded - Work to Commence | 30-Jul-20  | -                    | -                         | M/s Dineshchandra R. Agrawal Infracon Pvt. Ltd.                                                     | -                     |
| 3                                      | Haryana        | Pkg 3   | 33.000   | 59.063  | 26          | Under Construction         | 07-Aug-20  | 14-May-21            | 15-May-23                 | M/s Dineshchandra R. Agrawal Infracon Pvt. Ltd.                                                     | -                     |
| <b>Delhi – Faridabad - Sohna Total</b> |                |         |          |         | <b>60</b>   |                            |            |                      |                           |                                                                                                     |                       |
| 1                                      | Haryana        | Pkg 1   | 0.000    | 18.460  | 18          | Under Construction         | 05-Mar-19  | 13-Sep-19            | 11-Sep-21                 | M/s APCO Infratech Pvt. Ltd.                                                                        | 57%                   |
| 2                                      | Haryana        | Pkg 2   | 18.460   | 46.960  | 29          | Under Construction         | 05-Mar-19  | 13-Sep-19            | 11-Sep-21                 | M/s APCO Infratech Pvt. Ltd.                                                                        | 49%                   |
| 3                                      | Haryana        | Pkg 3   | 46.960   | 78.760  | 32          | Under Construction         | 28-May-19  | 05-Sep-19            | 03-Sep-21                 | M/s Centrodorstroy India Pvt. Ltd.                                                                  | 77%                   |
| 4                                      | Rajasthan      | Pkg 4   | 78.760   | 115.660 | 37          | Under Construction         | 09-Mar-19  | 10-Dec-19            | 08-Dec-21                 | M/s H.G. Infra Engineering Limited                                                                  | 68%                   |
| 5                                      | Rajasthan      | Pkg 5   | 115.660  | 151.800 | 36          | Under Construction         | 09-Mar-19  | 10-Dec-19            | 08-Dec-21                 | M/s KCC Buildcon Pvt. Ltd.                                                                          | 58%                   |
| 6                                      | Rajasthan      | Pkg 6   | 151.800  | 182.960 | 31          | Under Construction         | 09-Mar-19  | 20-Nov-19            | 19-Nov-21                 | M/s KCC Buildcon Pvt. Ltd.                                                                          | 77%                   |
| 7                                      | Rajasthan      | Pkg 7   | 182.960  | 214.220 | 31          | Under Construction         | 28-May-19  | 07-Feb-20            | 06-Feb-22                 | M/s Gawar Constructions Ltd.                                                                        | 73%                   |
| 8                                      | Rajasthan      | Pkg 8   | 214.220  | 247.270 | 33          | Under Construction         | 11-Feb-20  | 07-Nov-20            | 06-Nov-22                 | M/s H.G. Infra Engineering Limited                                                                  | 27%                   |
| 9                                      | Rajasthan      | Pkg 9   | 247.270  | 292.910 | 46          | Under Construction         | 26-Feb-20  | 18-Dec-20            | 17-Dec-22                 | M/s H.G. Infra Engineering Limited                                                                  | 16%                   |
| 10                                     | Rajasthan      | Pkg 10  | 292.910  | 319.360 | 26          | Under Construction         | 30-Jun-20  | 22-May-21            | 21-May-23                 | M/s Dhaya Maju Infrastructure (Asia ) Sdn. Berhad - Crescent EPC Projects & Technical Services Ltd. | -                     |
| 11                                     | Rajasthan      | Pkg 11  | 319.360  | 330.990 | 12          | Under Construction         | 19-Jun-20  | 22-May-21            | 21-May-23                 | M/s Larsen & Toubro Ltd.                                                                            | -                     |
| 12                                     | Rajasthan      | Pkg 12  | 330.990  | 359.130 | 28          | Under Construction         | 18-Jun-20  | 01-Apr-21            | 31-Mar-23                 | M/s G R Infraprojects Limited                                                                       | -                     |
| 13                                     | Rajasthan      | Pkg 13  | 359.130  | 388.380 | 29          | Under Construction         | 18-Jun-20  | 25-Mar-21            | 24-Mar-23                 | M/s CDS Infra Projects Limited                                                                      | -                     |
| 14                                     | Rajasthan      | Pkg 14  | 388.380  | 418.960 | 31          | Under Construction         | 30-Jun-20  | 24-May-21            | 23-May-23                 | M/s Dhaya Maju Infrastructure (Asia ) Sdn. Berhad - Crescent EPC Projects & Technical Services Ltd. | -                     |
| 15                                     | Rajasthan      | Pkg 15  | 418.960  | 427.260 | 8           | Awarded - Work to Commence | 22-Dec-20  | -                    | -                         | M/s Dilip Buildcon Ltd – M/s Altis Holding Corporation                                              | -                     |
| 16                                     | Rajasthan      | Pkg 16  | 427.260  | 452.390 | 25          | Under Construction         | 08-Jul-20  | 05-Jan-21            | 04-Jan-23                 | M/s Dineshchandra R. Agrawal Infracon Pvt. Ltd.                                                     | 7%                    |
| 17                                     | Madhya Pradesh | Pkg 17  | 452.390  | 484.390 | 32          | Under Construction         | 11-Feb-20  | 08-Oct-20            | 07-Oct-22                 | M/s JiangXi Construction Engineering (Group)                                                        | 29%                   |

| #                             | State          | Package | Chainage |         | Length (km) | Status                     | Award Date | Date of Commencement | Scheduled Completion Date | Concessionaire                                                                               | Physical Progress (%) |
|-------------------------------|----------------|---------|----------|---------|-------------|----------------------------|------------|----------------------|---------------------------|----------------------------------------------------------------------------------------------|-----------------------|
|                               |                |         | From     | To      |             |                            |            |                      |                           |                                                                                              |                       |
|                               |                |         |          |         |             |                            |            |                      |                           | Corporation Ltd. - MKC Infrastructure Ltd. (JV)                                              |                       |
| 18                            | Madhya Pradesh | Pkg 18  | 484.390  | 517.390 | 33          | Under Construction         | 01-Oct-19  | 07-Feb-20            | 06-Feb-22                 | M/s G R Infraprojects Limited                                                                | 52%                   |
| 19                            | Madhya Pradesh | Pkg 19  | 517.390  | 546.890 | 30          | Under Construction         | 11-Feb-20  | 05-Nov-20            | 04-Nov-22                 | M/s JiangXi Construction Engineering (Group) Corporation Ltd. - MKC Infrastructure Ltd. (JV) | 10%                   |
| 20                            | Madhya Pradesh | Pkg 20  | 546.890  | 572.190 | 25          | Under Construction         | 08-Mar-19  | 06-Dec-19            | 05-Dec-21                 | M/s GHV (India) Pvt Ltd.                                                                     | 40%                   |
| 21                            | Madhya Pradesh | Pkg 21  | 572.190  | 602.390 | 30          | Under Construction         | 28-May-19  | 10-Dec-19            | 09-Dec-21                 | M/s G R Infraprojects Limited                                                                | 56%                   |
| 22                            | Madhya Pradesh | Pkg 22  | 602.390  | 627.390 | 25          | Under Construction         | 19-Jun-20  | 20-Nov-20            | 19-Nov-22                 | M/s Larsen & Toubro Ltd.                                                                     | 26%                   |
| 23                            | Madhya Pradesh | Pkg 23  | 627.390  | 652.690 | 25          | Under Construction         | 07-Aug-19  | 29-May-20            | 28-May-22                 | M/s G R Infraprojects Limited                                                                | 37%                   |
| 24                            | Madhya Pradesh | Pkg 24  | 652.690  | 673.740 | 21          | Under Construction         | 07-Aug-19  | 05-Mar-20            | 04-Mar-22                 | M/s G R Infraprojects Limited                                                                | 49%                   |
| 25                            | Madhya Pradesh | Pkg 25  | 673.740  | 696.890 | 23          | Under Construction         | 07-Aug-19  | 05-Mar-20            | 04-Mar-22                 | M/s G R Infraprojects Limited                                                                | 45%                   |
| 26                            | Gujarat        | Pkg 26  | 696.890  | 726.390 | 30          | Under Evaluation           | -          | -                    | -                         | -                                                                                            | -                     |
| 27                            | Gujarat        | Pkg 27  | 726.390  | 755.390 | 29          | Under Evaluation           | -          | -                    | -                         | -                                                                                            | -                     |
| 28                            | Gujarat        | Pkg 28  | 755.390  | 780.890 | 26          | Awarded - Work to Commence | 27-May-21  | -                    | -                         | M/s GHV (India) Pvt Ltd                                                                      | -                     |
| 29                            | Gujarat        | Pkg 29  | 780.890  | 803.390 | 23          | Under Construction         | 23-Jul-20  | 16-Apr-21            | 15-Apr-21                 | M/s PNC Infratech Pvt. Ltd.                                                                  | -                     |
| 30                            | Gujarat        | Pkg 30  | 803.390  | 824.890 | 22          | Awarded - Work to Commence | 05-Oct-20  | -                    | -                         | M/s Patel Infrastructure Limited                                                             | -                     |
| 31                            | Gujarat        | Pkg 31  | 824.890  | 844.350 | 19          | Under Construction         | 23-Jul-20  | 18-May-21            | 17-May-21                 | M/s PNC Infratech Pvt. Ltd.                                                                  | -                     |
| <b>Delhi – Vadodara Total</b> |                |         |          |         | <b>844</b>  |                            |            |                      |                           |                                                                                              |                       |
| 1                             | Gujarat        | Pkg 1   | 355.000  | 378.740 | 24          | Under Construction         | 20-Mar-18  | 18-Jan-19            | 17-Jun-21                 | M/s IRB Infrastructure Developers Ltd.                                                       | 73%                   |
| 2                             | Gujarat        | Pkg 2   | 323.000  | 355.000 | 32          | Under Construction         | 28-Mar-18  | 31-Jan-19            | 30-Jun-21                 | M/s IRCON International Limited                                                              | 76%                   |
| 3                             | Gujarat        | Pkg 3   | 292.000  | 323.000 | 31          | Under Construction         | 28-Mar-18  | 08-Mar-19            | 07-Jun-21                 | M/s Patel Infrastructure Limited                                                             | 78%                   |
| 4                             | Gujarat        | Pkg 4   | 279.000  | 292.000 | 13          | Under Construction         | 28-Mar-18  | 10-Dec-18            | 08-Jun-21                 | M/s Ashoka Buildcon Limited                                                                  | 87%                   |
| 5                             | Gujarat        | Pkg 5   | 254.430  | 279.000 | 25          | Under Construction         | 28-Mar-18  | 01-Nov-19            | 31-Oct-21                 | M/s Sadbhav Engineering Pvt. Ltd.                                                            | 8%                    |
| 6                             | Gujarat        | Pkg 6   | 217.500  | 254.430 | 37          | Awarded - Work to Commence | 30-Jul-20  | -                    | -                         | M/s G R Infraprojects Limited                                                                | -                     |

| #                      | State       | Package               | Chainage |         | Length<br>(km) | Status                     | Award Date | Date of Commencement | Scheduled Completion Date | Concessionaire                         | Physical Progress (%) |
|------------------------|-------------|-----------------------|----------|---------|----------------|----------------------------|------------|----------------------|---------------------------|----------------------------------------|-----------------------|
|                        |             |                       | From     | To      |                |                            |            |                      |                           |                                        |                       |
| 7                      | Gujarat     | Pkg 7                 | 190.000  | 217.500 | 28             | Awarded - Work to Commence | 31-Jul-20  | -                    | -                         | M/s IRB Infrastructure Developers Ltd. | -                     |
| 8                      | Gujarat     | Pkg 8                 | 154.600  | 190.000 | 35             | Awarded - Work to Commence | 27-May-21  | -                    | -                         | M/s Roadway Solutions India Infra Ltd. | -                     |
| 9                      | Gujarat     | Pkg 9                 | 128.000  | 154.600 | 27             | Under Evaluation           | -          | -                    | -                         | -                                      | -                     |
| 10                     | Gujarat     | Pkg 10                | 103.400  | 128.000 | 25             | Awarded - Work to Commence | 30-Mar-21  | -                    | -                         | M/s Roadway Solutions India Infra Ltd. | -                     |
| 11                     | Maharashtra | Pkg 11                | 77.000   | 103.400 | 26             | Awarded - Work to Commence | 15-Oct-20  | -                    | -                         | M/s RKC Infrabuilt Private Ltd.        | -                     |
| 12                     | Maharashtra | Pkg 12                | 50.700   | 77.000  | 26             | Awarded - Work to Commence | 15-Oct-20  | -                    | -                         | M/s Montecarlo Limited                 | -                     |
| 13                     | Maharashtra | Pkg 13                | 26.582   | 50.700  | 24             | Awarded - Work to Commence | 15-Oct-20  | -                    | -                         | M/s G R Infraprojects Ltd.             | -                     |
|                        |             | Pkg 13 (Spur to JNPT) | 0.000    | 3.000   | 3              |                            |            | -                    | -                         |                                        | -                     |
| Vadodara – Virar Total |             |                       |          |         | 354            |                            |            |                      |                           |                                        | -                     |
| 1                      | Maharashtra | Pkg 14 (Spur to JNPT) | 3.000    | 20.200  | 17             | Under Bidding              | -          | -                    | -                         | -                                      | -                     |
| 2                      | Maharashtra | Pkg 15 (Spur to JNPT) | 20.200   | 43.000  | 23             | Under Bidding              | -          | -                    | -                         | -                                      | -                     |
| 3                      | Maharashtra | Pkg 16 (Spur to JNPT) | 43.000   | 69.700  | 27             | Under Bidding              | -          | -                    | -                         | -                                      | -                     |
| 4                      | Maharashtra | Pkg 17 (Spur to JNPT) | 69.700   | 79.780  | 10             | Under Bidding              | -          | -                    | -                         | -                                      | -                     |
| 5                      | Maharashtra | Pkg 18 (Spur to JNPT) | 79.780   | 94.290  | 15             | DPR in Progress            | -          | -                    | -                         | -                                      | -                     |
| Virar – JNPT Total     |             |                       |          |         | 92             |                            |            |                      |                           |                                        |                       |
| Delhi - Mumbai Total   |             |                       |          |         | 1350           |                            |            |                      |                           |                                        | -                     |
